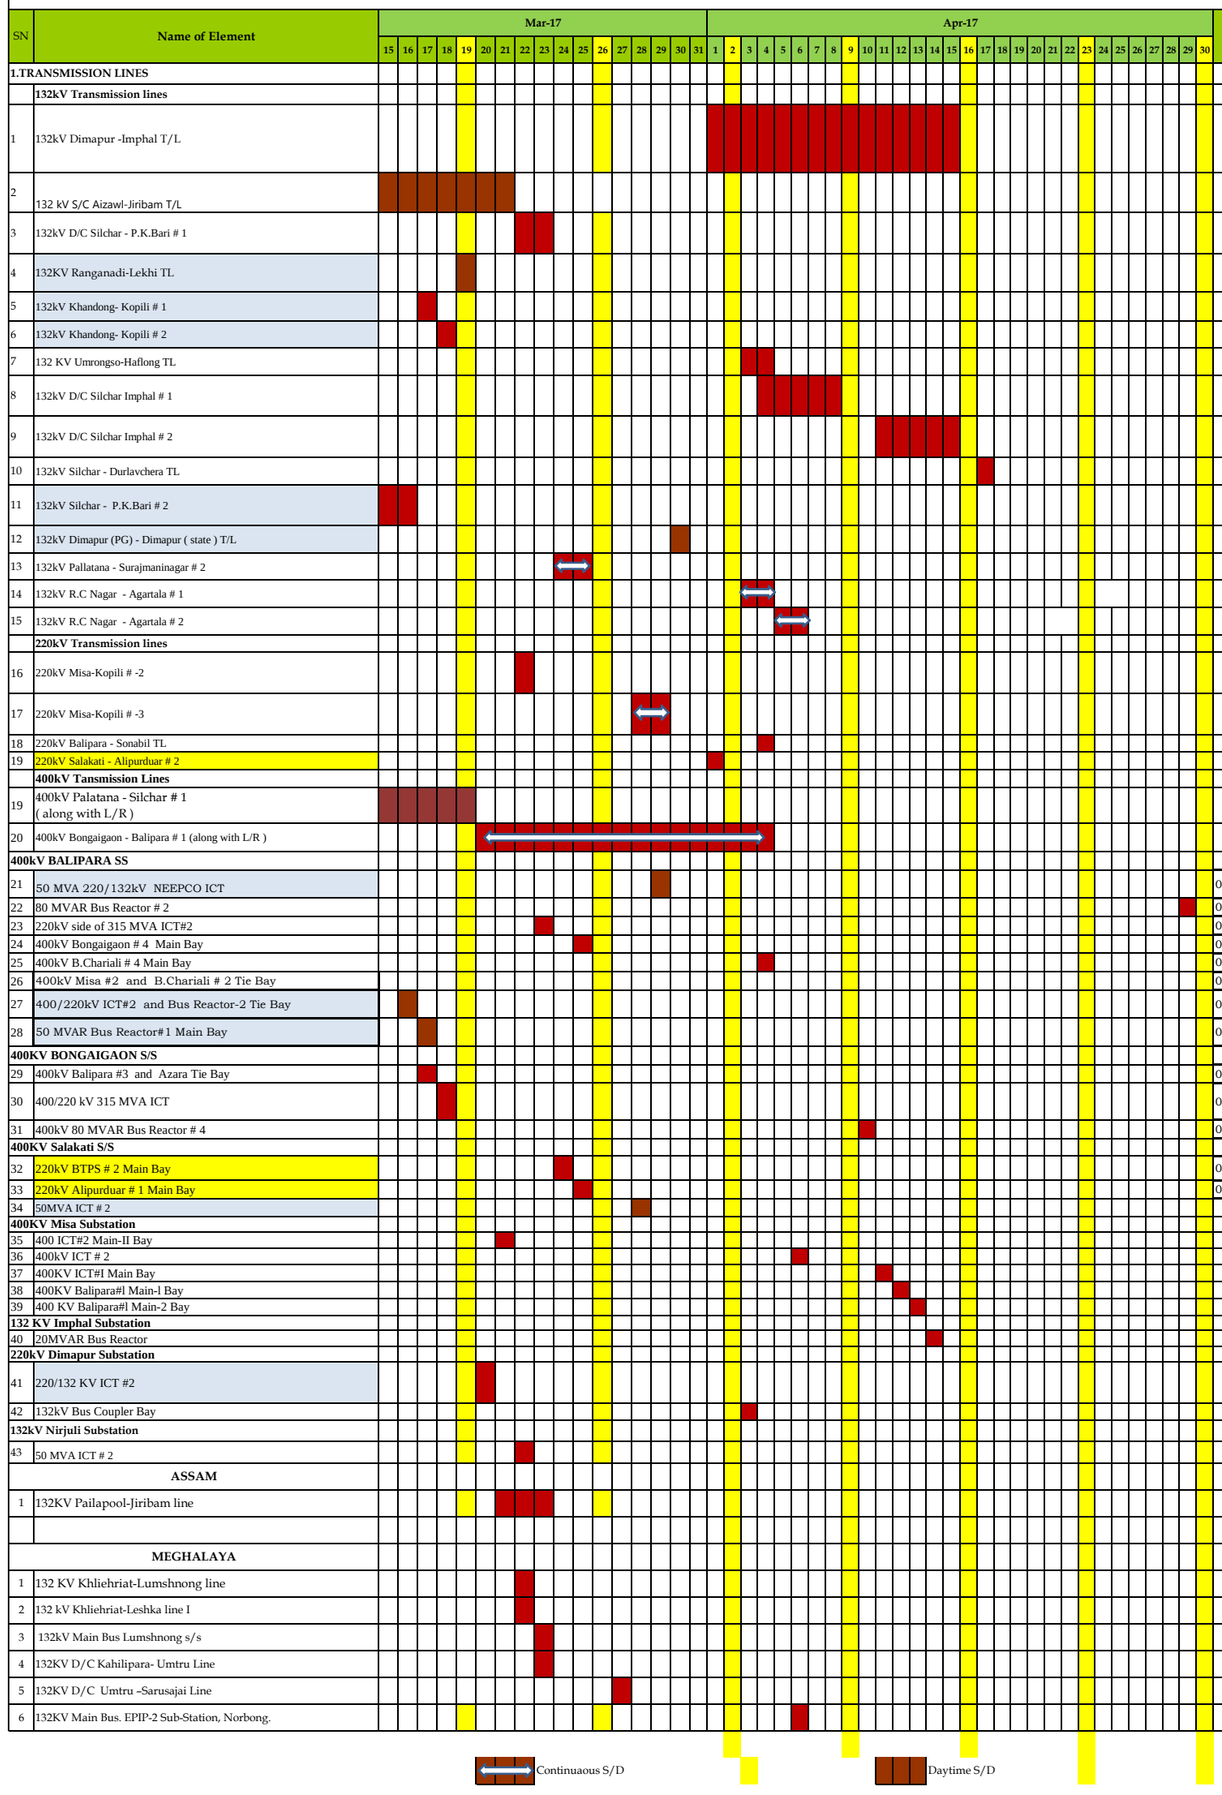SN	Name of Element	Time	
1.TRANSMISSION LINES			
	132kV Transmission lines		
1	132kV Dimapur -Imphal T/L	08:00 to 16:00	1. Mass replacement of all existing insulators with polymer composite long rod insulators in line with decision of 15th NERPC meeting (Day time SD) (Rescheduled already approved S/D in last OCC) . 2. Shifting of velnerable tower location 271 affected by landslide. **This work is likely to be affected by ongoing economic blokade in Manipur**
2	132 kV S/C Aizawl-Jiribam T/L	08:00 to 16:00	Mass replacement of all existing insulators with polymer composite long rod insulators in line with decision of 15th NERPC meeting (Day time SD) (already approved S/D in last OCC)
3	132kV D/C Silchar - P.K.Bari # 1	09:00 to 16:00	Execution of jumper tightening , tower parts refitting (theft) in areas with acute ROW issues under security coverage provided by administration (Resceduled earlier approved S/D in last OCC)
4	132KV Ranganadi-Lekhi TL	07:00 to 16:00	Termination of LILO of 132KV SC NDTL at Pare HEP (NEEPCO) & woks to be carried out in between Loc no 43 to 45 of NDTL . (already approved S/D in last OCC)
5	132kV Khandong- Kopili # 1	08:00 to 16:00	CB timing , replacement of limit swiches at kopili , S/D of line taken due to absence of transfer bus scheme at kopili. (already approved S/D in last OCC)
6	132kV Khandong- Kopili # 2	08:00 to 16:00	CB timing, Replcaement of defective trip coil of CB at kopili , S/D of line taken due to absence of transfer bus scheme at kopili. (already approved S/D in last OCC)
7	132 KV Umrongso-Haflong TL	11:00 to 14:00	Stringing of OPGW at river crossing having 1200 metre long span(Loc No. 131-132) , Daytime S/D .
8	132kV D/C Silchar Imphal # 1	09:00 to 16:00	For shifting of tower including Tower erection,Destringing,Restringing & Dismantling etc at Loc.No.244/0 (DC+0) & Loc.No.289B/0 (DD+0) . **This work is likely to be affected by ongoing economic blokade in Manipur .**
9	132kV D/C Silchar Imphal # 2	09:00 to 16:00	For shifting of tower including Tower erection,Destringing,Restringing & Dismantling etc at Loc.No.244/0 (DC+0) & Loc.No.289B/0 (DD+0) .**This work is likely to be affected by ongoing economic blokade in Manipur .**
10	132kV Silchar - Durlavchera TL	09:00 to 16:00	Annual Bay Maintenance of Bay equipments
11	132kV Silchar - P.K.Bari # 2	08:00 to 16:00	Execution of jumper tightening , tower parts refitting (theft) in areas with acute ROW issues under security under security coverage provided by administration. (already approved S/D in last OCC)
12	132kV Dimapur (PG) - Dimapur (state) T/L	08:00 to 16:00	AMP of Bay equipments at Dimapur Powergrid S/S.(already approved S/D in last OCC)
13	132kV Pallatana - Surajmaninagar # 2	08:00 to 16:00	Installation of CT's for uprating of CT ratio for accomodation higher power flow as per requirement of constituents. (continuous S/D)
14	132kV R.C Nagar - Agartala # 1	08:00 to 16:00	Installation of CT's for uprating of CT ratio for accomodation higher power flow as per requirement of constituents. (continuous S/D)
15	132kV R.C Nagar - Agartala # 2	08:00 to 16:00	Installation of CT's for uprating of CT ratio for accomodation higher power flow as per requirement of constituents. (continuous S/D)
	220kV Transmission lines		
16	220kV Misa-Kopili # -2	08:00 to 16:00	Jungle clearing against growth of eucaliptus trees between Loc.313 and 314 (The locations are under jurisdiction of forest department and the work shall be caried out in presence of forest officials)
17	220kV Misa-Kopili # -3	08:00 to 16:00	CVT and LA of 220kV Misa-Kopili-3 line at Kopili S/S end is required to be shifted for accommodating new GIS Building being constructed at Kopili S/S under NERSS-III Scheme (Continuous Shutdown)
18	220kV Balipara - Sonabil TL	08:00 to 16:00	Annual Bay Maintenance of Bay equipments.
19	220kV Salakati - Alipurduar # 2	09:00 to 10:00	Arresting R-ph CVT oil leakage at Salakati
	400kV Tansmission Lines		
19	400kV Palatana - Silchar # 1 (along with L/R)	08:00 to 21:00	Piling work for tower foundation i.r.f. GIS package extension work arround Pallatana-1 main and tie bay .(system upgradation, Daytime S/D) (already approved S/D in last OCC)
20	400kV Bongaigaon - Balipara # 1 (along with L/R)	08:00 to 16:00	Continuous S/D required for modification in swichyard layout for enabling Line Reactor to Bus reactor (swichable reactor) at Bongaigaon end.
400kV BALIPARA SS			
21	50 MVA 220/132kV NEEPCO ICT	07:00 to 16:00	Annual Maintenance work , ICT will be out of service (already approved S/D in last OCC)
22	80 MVAR Bus Reactor # 2	08:00 to 16:00	Annual Maintenance work , BR will be out of service
23	220kV side of 315 MVA ICT#2	08:00 to 16:00	Annual Maintenance work , No outage of element.
24	400kV Bongaigaon # 4 Main Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
25	400kV B.Chariali # 4 Main Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
26	400kV Misa #2 and B.Chariali # 2 Tie Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
27	400/220kV ICT#2 and Bus Reactor-2 Tie Bay	07:00 to 16:00	Annual Maintenance work , No outage of element (already approved S/D in last OCC)
28	50 MVAR Bus Reactor#1 Main Bay	07:00 to 16:00	Annual Maintenance work , No outage of element (already approved S/D in last OCC)
400KV BONGAIGAON S/S			
29	400kV Balipara #3 and Azara Tie Bay	09:00 to 16:00	Annual Maintenance work , No outage of element.
30	400/220 kV 315 MVA ICT	09:00 to 16:00	S/D of ICT requested for spare bus dismantling work against GIS construction activity (system upgradation).
31	400kV 80 MVAR Bus Reactor # 4	09:00 to 11:00	Annual Maintenance work in CB , BR will be out of service
400KV Salakati S/S			
32	220kV BTPS # 2 Main Bay	09:00 to 16:00	Annual Maintenance work , No outage of element.
33	220kV Alipurduar # 1 Main Bay	09:00 to 16:00	Annual Maintenance work , No outage of element.
34	50MVA ICT # 2	08:00 to 16:00	AMP of Bay equipments and ICT (already approved S/D in last OCC)
400KV Misa Substation			
35	400 ICT#2 Main-II Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
36	400kV ICT # 2	08:00 to 16:00	AMP of Bay equipments and ICT , ICT shall remain out of service .
37	400KV ICT#I Main Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
38	400KV Balipara#l Main-l Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
39	400 KV Balipara#l Main-2 Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
132 KV Imphal Substation			
40	20MVAR Bus Reactor	08:00 to 16:00	AMP of Bay equipments and Reactor
220kV Dimapur Substation			
41	220/132 KV ICT #2	08:00 to 16:00	Annual Mainetance of Bay equipments and ICT (Resceduled S/D , already approved S/D in last OCC)
42	132kV Bus Coupler Bay	08:00 to 16:00	Annual Maintenance work , No outage of element.
132kV Nirjuli Substation			
43	50 MVA ICT # 2		
	ASSAM		
1	132KV Pailapool-Jiribam line	10:00 to 16:00	For Jungle cutting works as per revise schedule due to ongoing HSLC Examination.
	MEGHALAYA		
1	132 KV Khliehriat-Lumshnong line	10:30 to 14:30	Replacing of broken disc at Loc. No. 225 (Myndihati)
2	132 kV Khliehriat-Leshka line I	10:00 to13:00	For maintenance work of terminal equipments
3	132kV Main Bus Lumshnong s/s	11:00 to 15:00	For maintenance work of terminal equipments
4	132KV D/C Kahilipara- Umtru Line	09:00 to 16:00	Jungle Clearing
5	132KV D/C Umtru –Sarusajai Line	09:00 to 16:00	Jungle Clearing
6	132KV Main Bus. EPIP-2 Sub-Station, Norbong.	10:00 to 15:00	General maintenance
